



འབྲུག་རྒྱལ་ཁབ་ལ་ལོ་རྒྱུ་ལྷན་ཁག་ རྒྱལ་ཁབ་ཤུག་ལྷན་ཁག་གི་འཕྲིན།
 Ministry of Energy and Natural Resources
 Royal Government of Bhutan
Bhutan Power System Operator
 Thimphu: Bhutan



THE DAILY BHUTAN POWER SYSTEM OPERATOR LOAD-GENERATION BALANCE REPORT & ENERGY FIGURES ISSUED ON 09-Feb-2026(=vcimport, +ve=export)							
Report Details	Date	Time	National Coincidental Peak Load (MW)		Date	Time	Load
	February 8, 2026	9:00 AM			08-Nov-25	19:03:00	1,477.00
Sl.No.	Hydropower Plant	Unit	MW	Transmission Lines and Elements	Load (MW)	Remarks	
1	6 x 170MW THP	Unit-I	187.34	400kV THP - Siliguri Line - I	0.00	Unit- IV, V & VI under Shutdown (Annual Maintenance). 400kV THP_SIL line I on Standby.	
		Unit-II	187.55	400kV THP - Siliguri Line - II	81.98		
		Unit-III	186.73	400kV THP - Norbugang - IV	154.88		
		Unit-IV	0.00	400kV THP - Malbase Line - III	320.18		
		Unit-V	0.00	400kV Malbase - Siliguri Line	21.32		
		Unit-VI	0.00	400kV Norbugang-Siliguri Line	-2.84		
		Total	561.62	Auxiliary Consumption & Transformation Losses at Generator end	0.82%		
2	4 x 180MW MHP	Unit-I	185.82	400kV MHP - Jigmeling Line - I	0.00	Unit-IV under Shutdown (Annual Maintenance). Unit-III under Shutdown. 400kV MHP-JIG Line - I under Shutdown & line III on Standby as other two lines can cater the load.	
		Unit-II	185.86	400kV MHP - Jigmeling Line - II	122.10		
		Unit-III	0.00	400kV MHP - Jigmeling Line - III	0.00		
		Unit-IV	0.00	400kV MHP - Jigmeling Line - IV	122.84		
		-	-	220kV Jigmeling - BitDeer Line - I	197.60		
		-	-	220kV Jigmeling - BitDeer Line - II	191.21		
		-	-	500MVA, 400/220kV ICT at Jigmeling (HV)	446.91		
		-	-	400kV Jigmeling - Alipurduar Line - I	-15.27		
		-	-	400kV Jigmeling - Alipurduar Line - II	-16.73		
		-	-	80MVA, 220/132kV ICT - I (HV)	-31.19		
		-	-	80MVA, 220/132kV ICT - II (HV)	-30.86		
		-	-	132kV MHP - Yurmo Line - II	63.96		
		-	-	132kV MHP - Tintibi Line	80.02		
		-	-	132kV Gelephu - Salakati Line	-48.63		
		Total	371.68	Auxiliary Consumption & Transformation Losses at Generator end	0.68%		
3	6 x 170MW PHP-II	Unit-I	0.00	400kV PHP II - Jigmeling - I	173.10	Unit-I, II & IV under Shutdown (Annual Maintenance). 400kV PHP II-Jigmeling-II & 400kV PHP II-Alipurduar line-I on standby. Unit-III on Standby.	
		Unit-II	0.00	400kV PHP II - Jigmeling -II	0.00		
		Unit-III	0.00	400kV PHP II - Alipurduar - I	0.00		
		Unit-IV	0.00	400kV PHP II - Alipurduar - II	72.30		
		Unit-V	124.70	-	-		
		Unit-VI	119.90	-	-		
		Total	244.60	Auxiliary Consumption & Transformation Losses at Generator end	-0.33%		
4	4 x 84MW CHP	Unit-I	0.00	220kV CHP - Birpara Line - I	-66.65	Unit-I & II under Shutdown (Annual Maintenance). 220kV CHP-Birpara Line-II under Shutdown.	
		Unit-II	0.00	220kV CHP - Birpara Line - II	0.00		
		Unit-III	84.33	220kV CHP - Gedu	-90.40		
		Unit-IV	80.43	220kV CHP - Jamjee - I	107.57		
		-	-	220kV CHP - Jamjee - II	107.26		
		-	-	220kV CHP - Jamjee - III	103.43		
		-	-	220kV Malbase - Birpara Line	-19.45		
		-	-	66kV CHP - Gedu Line	4.13		
		Total	164.76	Auxiliary Consumption & Transformation Losses at Generator end	-0.35%		
5	2 x 12MW BHP (U/S)	Unit-I	5.80	220kV BHP - Semtokha Line	24.07	L/S Unit-I under AMP. U/S Unit-II under Shutdown.	
		Unit-II	0.00	66kV BHP - Lobeysa Line	19.04		
		Total	5.80	220kV BHP - Tsirang Line	-25.88		
6	2 x 20MW BHP (L/S)	Unit-I	0.00	5MVA, 66/11kV TFR	0.58		
		Unit-II	11.90	30MVA ICT, 220/66kV (HV)	14.07		
		Total	11.90	Auxiliary Consumption & Transformation Losses at Generator end	-0.62%		
7	2 x 63MW DHP	Unit-I	0.00	220kV DHP - Tsirang Line	0.00	Total Plant Shutdown from 10:27 hrs (09.10.2025) due to Seepage in HRC .	
		Unit-II	0.00	220kV DHP - Dagapela Line	0.00		
		-	-	220kV BitDeer - Dagapela Line	58.21		
		Total	0.00	5MVA, 220/33kV TFR	0.00		
8	4 x 15MW KHP	Unit-I	12.19	132kV KHP - Nangkhor Line	9.80	Unit-II under AMP. Unit-III under Shutdown.	
		Unit-II	0.00	132kV KHP - Kilikhar Line	13.79		
		Unit-III	0.00	5MVA, 132/11kV TFR	0.52		
		Unit-IV	12.20	132kV Motanga - Rangia Line	8.32		
		Total	24.39	Auxiliary Consumption & Transformation Losses at Generator end	1.15%		
9	2 x 59MW NHP	Unit-I	0.00	132kV NHP-MHP-I	0.00	Unit I under Shutdown. 132kV NHP-MHP line I under ideal charge at NHP end.	
		Unit-II	20.02	132kV NHP-MHP-II	19.78		
		Total	20.02	Auxiliary Consumption & Transformation Losses at Generator end	1.20%		
10	2 x 9MW SHP	Unit-I	4.00	66kV SHP-Damdhum (Samtse)	0.00	Unit-II on Standby. Interim measure: Evacuation is through 33kV System.	
		Unit-II	0.00	-	-		
		Total	4.00	Auxiliary Consumption & Transformation Losses at Generator end	100.00%		
11	17.38 MWp Sephu (Solar)	Inverter-1	0.80	33kV SSP-Wangdue	3.73	33kV SSP-Trongsa Shutdown availed by BPC.	
		Inverter-2	1.34	33kV SSP-Trongsa	3.05		
		Inverter-3	1.59	-	-		
		Inverter-4	1.67	-	-		
		Inverter-5	1.38	-	-		
		Total	6.78	Auxiliary Consumption & Transformation Losses at Generator end	0.00%		

Note: Generation-Load Summary (MW) for 08-Feb-26 at 09:00 hrs

Sl. No.	Region	Total Generation	Total Domestic Load (Total Generation - Total Export)	Total Export(+ve)/ Import(-ve)
1	Both Eastern & Western (Whole Bhutan)	1,415.55	1,401.20	14.35

Note: Generation-Load Summary (MW) for 08-Feb-25 at 09:00 hrs

Sl. No.	Region	Total Generation	Total Domestic Load (Total Generation - Total Export)	Total Export(+ve)/ Import(-ve)
1	Both Eastern & Western (Whole Bhutan)	914.45	881.88	32.57

09:00 hrs Statistical Comparison (MW) for this and last year



THE DAILY BHUTAN POWER SYSTEM OPERATOR LOAD-GENERATION BALANCE REPORT & ENERGY FIGURES ISSUED ON 09-Feb-2026(-ve:import, +ve:export)

Report Details	Date	Time	National Coincidental Peak Load (MW)		Date	Time	Load
	February 8, 2026	18:00:00			08-Nov-25	19:03:00	1,477.00
Sl. No.	Hydropower Plant	Unit	MW	Transmission Lines and Elements	Load (MW)	Remarks	
1	6 x 170MW THP	Unit-I	40.64	400kV THP - Siliguri Line - I	0.00	Unit-IV, V & VI under Shutdown (Annual Maintenance). 400kV THP_SIL line I Under Shutdown.	
		Unit-II	40.79	400kV THP - Siliguri Line - II	-89.77		
		Unit-III	20.63	400kV THP - Norbugang Line - IV	41.50		
		Unit-IV	0.00	400kV THP - Malbase Line - III	149.16		
		Unit-V	0.00	400kV Malbase - Siliguri Line	-132.67		
		Unit-VI	0.00	400kV Norbugang-Siliguri Line	-123.89		
		Total	102.06	Auxiliary Consumption & Transformation Losses at Generator end	1.15%		
2	4 x 180MW MHP	Unit-I	20.19	400kV MHP - Jigmeling Line - I	0.00	Unit-III under Shutdown. Unit-IV under AMP. 400kV MHP-JLG Line - III on Standby. 400kV MHP-JLG line - I under Shutdown.	
		Unit-II	20.82	400kV MHP - Jigmeling Line - II	-31.70		
		Unit-III	0.00	400kV MHP - Jigmeling Line - III	0.00		
		Unit-IV	0.00	400kV MHP - Jigmeling Line - IV	-31.96		
		-	-	220kV Jigmeling - BitDeer Line - I	57.16		
		-	-	220kV Jigmeling - BitDeer Line - II	0.00		
		-	-	500MVA, 400/220kV ICT at Jigmeling (HV)	438.91		
		-	-	400kV Jigmeling - Alipurduar Line - I	-160.73		
		-	-	400kV Jigmeling - Alipurduar Line - II	-161.46		
		-	-	80MVA, 220/132kV ICT - I (HV)	-23.75		
		-	-	80MVA, 220/132kV ICT - II (HV)	-23.50		
		-	-	132kV MHP - Yurmo Line - II	68.38		
		-	-	132kV MHP - Tintibi Line	55.25		
		-	-	132kV Gelephu - Salakati Line	-71.13		
		Total	41.01	Auxiliary Consumption & Transformation Losses at Generator end	1.98%		
3	6 x 170MW PHP-II	Unit-I	0.00	400kV PHP II - Jigmeling -I	177.25	Unit-I, II & IV under Shutdown (Annual Maintenance). Unit-III on Standby. 400kV PHPII - JLG-II & 400kV PHPII - ALI-I on Standby.	
		Unit-II	0.00	400kV PHP II - Jigmeling -II	0.00		
		Unit-III	0.00	400kV PHP II - Alipurduar -I	0.00		
		Unit-IV	0.00	400kV PHP II - Alipurduar -II	-66.30		
		Unit-V	0.00	-	-		
		Unit-VI	110.82	-	-		
		Total	110.82	Auxiliary Consumption & Transformation Losses at Generator end	-0.12%		
4	4 x 84MW CHP	Unit-I	0.00	220kV CHP - Birpara Line - I	-114.19	Unit-I & II under Shutdown (Annual Maintenance). 220kV CHP_Birpara Line II under Shutdown.	
		Unit-II	0.00	220kV CHP - Birpara Line - II	0.00		
		Unit-III	49.32	220kV CHP - Gedu	-127.34		
		Unit-IV	53.64	220kV CHP - Jamjee - I	113.94		
		-	-	220kV CHP - Jamjee - II	113.20		
		-	-	220kV CHP - Jamjee - III	113.10		
		-	-	220kV Malbase - Birpara Line	-69.17		
-	-	66kV CHP - Gedu Line	3.18				
Total	102.96	Auxiliary Consumption & Transformation Losses at Generator end	1.04%				
5	2 x 12MW BHP (U/S)	Unit-I	5.70	220kV BHP - Semtokha Line	32.90	L/S Unit-I under AMP. U/S unit-II under Shutdown.	
		Unit-II	0.00	66kV BHP - Lobeyasa Line	23.19		
		Total	5.70	220kV BHP - Tsirang Line	-39.19		
6	2 x 20MW BHP (L/S)	Unit-I	0.00	5MVA, 66/11kV TFR	0.83		
		Unit-II	11.80	30MVA ICT, 220/66kV (HV)	18.37		
		Total	11.80	Auxiliary Consumption & Transformation Losses at Generator end	-1.31%		
7	2 x 63MW DHP	Unit-I	0.00	220kV DHP - Tsirang Line	0.00	220kV DHP -Tsirang Line Opened at 16:46 hrs Total Plant Shutdown from 10:27 hrs (09.10.2025) due to Seepage in HRC .	
		Unit-II	0.00	220kV DHP - Dagapela Line	0.00		
		-	-	220kV BitDeer - Dagapela Line	58.83		
		-	-	5MVA, 220/33kV TFR	0.00		
		Total	0.00	Auxiliary Consumption & Transformation Losses at Generator end	0.00%		
8	4 x 15MW KHP	Unit-I	12.16	132kV KHP - Nangkor Line	8.65	Unit-III on Standby. Unit-II under Shutdown (AMP).	
		Unit-II	0.00	132kV KHP - Kilikhar Line	14.97		
		Unit-III	0.00	5MVA, 132/11kV TFR	0.50		
		Unit-IV	12.22	132kV Motanga - Rangia Line	-15.98		
		Total	24.38	Auxiliary Consumption & Transformation Losses at Generator end	1.07%		
9	2 x 59MW NHP	Unit-I	0.00	132kV NHP-MHP-I	0.00	Unit I under Shutdown 132kV NHP-MHP line I under ideal charge at NHP end.	
		Unit-II	20.00	132kV NHP-MHP-II	19.77		
		Total	20.00	Auxiliary Consumption & Transformation Losses at Generator end	1.15%		
10	2 x 9MW SHP	Unit-I	3.90	66kV SHP-Damdhum (Samtse)	0.00	Unit-II on Standby. Interim measure: Evacuation is through 33kV System.	
		Unit-II	0.00	-	-		
		Total	3.90	Auxiliary Consumption & Transformation Losses at Generator end	100.00%		

Note: Generation-Load Summary (MW) for 08-Feb-2026 at 18:00 hrs

Sl. No.	Region	Total Generation	Total Domestic Load (Total Generation - Total Export)	Total Export(+ve)/ Import(-ve)
1	Both Eastern & Western (Whole Bhutan)	422.63	1,427.92	-1,005.29


Note: Generation-Load Summary (MW) for 08-Feb-2025, at 18:00 hrs

Sl. No.	Region	Total Generation	Total Domestic Load (Total Generation - Total Export)	Total Export(+ve)/ Import(-ve)
1	Both Eastern & Western (Whole Bhutan)	936.46	906.62	29.84

Note: Daily Energy (MUs) and Power(MW) Statistics for 08-Feb-2026

Sl. No.	Total Energy Generation	Daily Energy Met	Net Energy Import (IEX and Solar)	Net Energy Export	Peak Cross-border (MW)
1	14.20	32.78	18.59	0.00	-1,050.42

19:00 hrs Statistical Comparison (MW) for this and last year

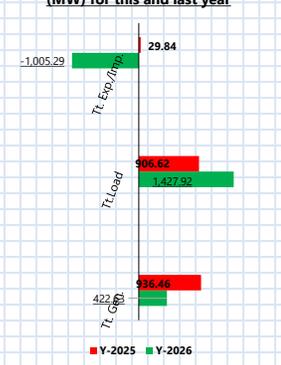

1. The instantaneous load balance does not tend towards zero. This could be due to the following reasons:
 i) Not all the meters are digital and nor are all the meter at all locations can be read at same time (say 9:00hrs) due to many meter to be read manually. ii) The clocks of all the locations are not synchronized.
 2. This report, compiled using the SCADA data, is prepared to give an overall idea of the generation & load flow for the system at a particular instant. This report also gives energy and import/export figures.
 3. When SCADA data are unavailable for certain stations due to technical issues, required data are collected from the site.
