



འབྲུག་གཞི་རིམ་ལྷན་ཁྲིམས་ཀྱི་འགན་ཁུར་ལྷན་ཁྲིམས་  
Ministry of Energy and Natural Resources  
Royal Government of Bhutan  
Bhutan Power System Operator  
Thimphu: Bhutan



THE DAILY BHUTAN POWER SYSTEM OPERATOR LOAD-GENERATION BALANCE REPORT & ENERGY FIGURES ISSUED ON 09-Mar-2026(-ve:import, +ve:export)

Report Details	Date	Time	National Coincidental Peak Load (MW)		Date	Time	Load
	March 8, 2026	9:00 AM			08-Nov-25	19:03:00	1,477.00
Sl.No.	Hydropower Plant	Unit	MW	Transmission Lines and Elements	Load (MW)	Remarks	
1	6 x 170MW THP	Unit-I	0.00	400kV THP - Siliguri Line - I	61.71	Unit-I, II & III (Penstock-I Shutdown). 400kV THP_SIL line II and 400kV Norbugang-Siliguri tripped and it's under inspection/Shutdown.	
		Unit-II	0.00	400kV THP - Siliguri Line - II	0.00		
		Unit-III	0.00	400kV THP - Norbugang - IV	147.43		
		Unit-IV	164.67	400kV THP - Malbase Line - III	290.84		
		Unit-V	169.98	400kV Malbase - Siliguri Line	9.50		
		Unit-VI	170.38	400kV Norbugang-Siliguri Line	0.00		
		<b>Total</b>	<b>505.03</b>	<b>Auxiliary Consumption &amp; Transformation Losses at Generator end</b>	<b>1.00%</b>		
2	4 x 180MW MHP	Unit-I	180.00	400kV MHP - Jigmeling Line - I	0.00	Unit-III & IV under Shutdown. 400kV MHP-JLG Line - II on Standby . 400kV MHP-JLG Line - I under Shutdown	
		Unit-II	179.91	400kV MHP - Jigmeling Line - II	0.00		
		Unit-III	0.00	400kV MHP - Jigmeling Line - III	126.46		
		Unit-IV	0.00	400kV MHP - Jigmeling Line - IV	126.43		
		-	-	220kV Jigmeling - BitDeer Line - I	202.24		
		-	-	220kV Jigmeling - BitDeer Line - II	178.00		
		-	-	500MVA, 400/220kV ICT at Jigmeling (HV)	414.55		
		-	-	400kV Jigmeling - Alipurduar Line - I	3.64		
		-	-	400kV Jigmeling - Alipurduar Line - II	2.18		
		-	-	80MVA, 220/132kV ICT - I (HV)	-17.55		
		-	-	80MVA, 220/132kV ICT - II (HV)	-17.37		
		-	-	132kV MHP - Yurno Line - II	62.43		
		-	-	132kV MHP - Tintibi Line	56.41		
		-	-	132kV Gelephu - Salakati Line	-56.19		
		<b>Total</b>	<b>360.71</b>	<b>Auxiliary Consumption &amp; Transformation Losses at Generator end</b>	<b>1.04%</b>		
3	6 x 170MW PHP-II	Unit-I	0.00	400kV PHP II - Jigmeling -I	171.14	Unit-I, II & IV under Shutdown (Annual Maintenance). Unit-III on Standby. 400kV PHPII - JLG-II on Standby. 400kV PHPII - ALI-II on standby.	
		Unit-II	0.00	400kV PHP II - Jigmeling -II	0.00		
		Unit-III	0.00	400kV PHP II - Alipurduar -I	90.00		
		Unit-IV	0.00	400kV PHP II - Alipurduar -II	0.00		
		Unit-V	130.41	-	-		
		Unit-VI	130.10	-	-		
		<b>Total</b>	<b>260.51</b>	<b>Auxiliary Consumption &amp; Transformation Losses at Generator end</b>	<b>-0.24%</b>		
4	4 x 84MW CHP	Unit-I	90.12	220kV CHP - Birpara Line - I	-38.47	Unit-II & IV under Shutdown (Annual Maintenance).	
		Unit-II	0.00	220kV CHP - Birpara Line - II	-38.33		
		Unit-III	90.07	220kV CHP - Gedu	-55.43		
		Unit-IV	0.00	220kV CHP - Jamjee - I	103.29		
		-	-	220kV CHP - Jamjee - II	103.03		
		-	-	220kV CHP - Jamjee - III	99.34		
		-	-	220kV Malbase - Birpara Line	-5.17		
		-	-	66kV CHP - Gedu Line	5.48		
		<b>Total</b>	<b>180.19</b>	<b>Auxiliary Consumption &amp; Transformation Losses at Generator end</b>	<b>0.71%</b>		
5	2 x 12MW BHP (U/S)	Unit-I	0.00	220kV BHP - Semtokha Line	22.41	L/S Unit-II under AMP. U/S Unit-I under AMP.	
		Unit-II	6.50	66kV BHP - Lobeyssa Line	17.88		
		<b>Total</b>	<b>6.50</b>	220kV BHP - Tsirang Line	-23.84		
6	2 x 20MW BHP (L/S)	Unit-I	10.67	5MVA, 66/11kV TFR	0.56	Total Plant Shutdown from 10:27 hrs (09.10.2025) due to Seepage in HRC . 220kV DHP-Dagapela line & 220kV DHP-Tsirang line on Standby.	
		Unit-II	0.00	30MVA ICT, 220/66kV (HV)	13.38		
		<b>Total</b>	<b>10.67</b>	<b>Auxiliary Consumption &amp; Transformation Losses at Generator end</b>	<b>0.93%</b>		
7	2 x 63MW DHP	Unit-I	0.00	220kV DHP - Tsirang Line	0.00		
		Unit-II	0.00	220kV DHP - Dagapela Line	0.00		
		-	-	220kV BitDeer - Dagapela Line	55.38		
		-	-	5MVA, 220/33kV TFR	0.00		
		<b>Total</b>	<b>0.00</b>	<b>Auxiliary Consumption &amp; Transformation Losses at Generator end</b>	<b>0.00%</b>		
8	4 x 15MW KHP	Unit-I	12.18	132kV KHP - Nangkor Line	10.86	Unit-II under AMP. Unit-III on Standby.	
		Unit-II	0.00	132kV KHP - Kikhar Line	12.97		
		Unit-III	0.00	5MVA, 132/11kV TFR	0.42		
		Unit-IV	12.18	132kV Motanga - Rangia Line	-11.06		
		<b>Total</b>	<b>24.36</b>	<b>Auxiliary Consumption &amp; Transformation Losses at Generator end</b>	<b>0.45%</b>		
9	2 x 59MW NHP	Unit-I	14.97	132kV NHP-MHP-I	14.78	Unit II under AMP. 132kV NHP-MHP line II under ideal charge at MHP end.	
		Unit-II	0.00	132kV NHP-MHP-II	0.00		
		<b>Total</b>	<b>14.97</b>	<b>Auxiliary Consumption &amp; Transformation Losses at Generator end</b>	<b>1.27%</b>		
10	2 x 9MW SHP	Unit-I	0.00	66kV SHP-Damdum (Samtse)	0.00	Unit-I on Standby. Interim measure: Evacuation is through 33kV System.	
		Unit-II	3.35	-	-		
		<b>Total</b>	<b>3.35</b>	<b>Auxiliary Consumption &amp; Transformation Losses at Generator end</b>	<b>100.00%</b>		
11	17.38 MWp Sephu (Solar)	Inverter-1	1.06	33kV SSP-Wangdue	5.41	All Inverter and 33kV Feedes are in service	
		Inverter-2	2.58	33kV SSP-Trongsang	4.80		
		Inverter-3	1.78	-	-		
		Inverter-4	2.38	-	-		
		Inverter-5	2.42	-	-		
		<b>Total</b>	<b>10.21</b>	<b>Auxiliary Consumption &amp; Transformation Losses at Generator end</b>	<b>0.00%</b>		


Note: Generation-Load Summary (MW) for 08-Mar-26 at 09:00 hrs

Sl. No.	Region	Total Generation	Total Domestic Load (Total Generation - Total Export)	Total Export(+ve)/ Import(-ve)
1	Both Eastern & Western (Whole Bhutan)	1,376.50	1,358.69	17.81

Note: Generation-Load Summary (MW) for 08-Mar-25 at 09:00 hrs

Sl. No.	Region	Total Generation	Total Domestic Load (Total Generation - Total Export)	Total Export(+ve)/ Import(-ve)
1	Both Eastern & Western (Whole Bhutan)	886.75	857.17	29.58

09:00 hrs Statistical Comparison (MW) for this and last year



**THE DAILY BHUTAN POWER SYSTEM OPERATOR LOAD-GENERATION BALANCE REPORT & ENERGY FIGURES ISSUED ON 09-Mar-2026(-ve:import, +ve:export)**

Report Details	Date	Time	National Coincidental Peak Load (MW)		Date	Time	Load
	March 8, 2026	18:00:00			08-Nov-25	19:03:00	1,477.00
Sl. No.	Hydropower Plant	Unit	MW	Transmission Lines and Elements	Load (MW)	Remarks	
1	6 x 170MW THP	Unit-I	0.00	400kV THP - Siliguri Line - I	-71.72	Unit-I, II & III (Penstock-I Shutdown). 400kV THP_SIL line II and 400kV Norbugang-Siliguri tripped and it's under inspection/Shutdown.	
		Unit-II	0.00	400kV THP - Siliguri Line - II	0.00		
		Unit-III	0.00	400kV THP - Norbugang Line - IV	141.44		
		Unit-IV	80.43	400kV THP - Malbase Line - III	170.94		
		Unit-V	80.22	400kV Malbase - Siliguri Line	-119.00		
		Unit-VI	80.23	400kV Norbugang-Siliguri Line	0.00		
		<b>Total</b>	<b>240.88</b>	<b>Auxiliary Consumption &amp; Transformation Losses at Generator end</b>	<b>0.09%</b>		
2	4 x 180MW MHP	Unit-I	65.91	400kV MHP - Jigmeling Line - I	0.00	Unit-III & IV under Shutdown. 400kV MHP-JLG Line - II on Standby 400kV MHP-JLG Line - I under Shutdown.	
		Unit-II	65.71	400kV MHP - Jigmeling Line - II	0.00		
		Unit-III	0.00	400kV MHP - Jigmeling Line - III	38.99		
		Unit-IV	0.00	400kV MHP - Jigmeling Line - IV	38.50		
		-	-	220kV Jigmeling - BitDeer Line - I	203.70		
		-	-	220kV Jigmeling - BitDeer Line - II	186.72		
		-	-	500MVA, 400/220kV ICT at Jigmeling (HV)	417.82		
		-	-	400kV Jigmeling - Alipurduar Line - I	-70.55		
		-	-	400kV Jigmeling - Alipurduar Line - II	-71.27		
		-	-	80MVA, 220/132kV ICT - I (HV)	-14.64		
		-	-	80MVA, 220/132kV ICT - II (HV)	-14.39		
		-	-	132kV MHP - Yurmo Line - II	6.53		
		-	-	132kV MHP - Tintibi Line	62.00		
		-	-	132kV Gelephu - Salakati Line	-56.19		
		<b>Total</b>	<b>131.62</b>	<b>Auxiliary Consumption &amp; Transformation Losses at Generator end</b>	<b>0.38%</b>		
3	6 x 170MW PHP-II	Unit-I	0.00	400kV PHP II - Jigmeling -I	207.54	Unit-I, II & IV under Shutdown (Annual Maintenance). Unit-V on Standby. 400kV PHPII - JLG-II on Standby. 400kV PHPII - ALI-II on Standby.	
		Unit-II	0.00	400kV PHP II - Jigmeling -II	0.00		
		Unit-III	120.33	400kV PHP II - Alipurduar -I	33.39		
		Unit-IV	0.00	400kV PHP II - Alipurduar -II	0.00		
		Unit-V	0.00	-	-		
		Unit-VI	120.37	-	-		
<b>Total</b>	<b>240.70</b>	<b>Auxiliary Consumption &amp; Transformation Losses at Generator end</b>	<b>-0.10%</b>				
4	4 x 84MW CHP	Unit-I	50.96	220kV CHP - Birpara Line - I	-72.32	Unit-II & IV under Shutdown (Annual Maintenance).	
		Unit-II	0.00	220kV CHP - Birpara Line - II	-71.72		
		Unit-III	50.03	220kV CHP - Gedu	-85.14		
		Unit-IV	0.00	220kV CHP - Jamjee - I	110.27		
		-	-	220kV CHP - Jamjee - II	109.50		
		-	-	220kV CHP - Jamjee - III	105.36		
		-	-	220kV Malbase - Birpara Line	-38.03		
-	-	66kV CHP - Gedu Line	4.67				
<b>Total</b>	<b>100.99</b>	<b>Auxiliary Consumption &amp; Transformation Losses at Generator end</b>	<b>0.37%</b>				
5	2 x 12MW BHP (U/S)	Unit-I	0.00	220kV BHP - Sementokha Line	43.44	L/S Unit-II under AMP. U/S unit-I under AMP.	
		Unit-II	5.50	66kV BHP - Lobeyasa Line	23.35		
		<b>Total</b>	<b>5.50</b>	220kV BHP - Tsirang Line	-51.46		
6	2 x 20MW BHP (L/S)	Unit-I	10.66	5MVA, 66/11kV TFR	0.68		
		Unit-II	0.00	30MVA ICT, 220/66kV (HV)	18.97		
		<b>Total</b>	<b>10.66</b>	<b>Auxiliary Consumption &amp; Transformation Losses at Generator end</b>	<b>0.93%</b>		
7	2 x 63MW DHP	Unit-I	0.00	220kV DHP - Tsirang Line	0.00	Total Plant Shutdown from 10:27 hrs (09.10.2025) due to Seepage in HRC . 220kV DHP-Dagapela line & 220kV DHP-Tsirang line on Standby.	
		Unit-II	0.00	220kV DHP - Dagapela Line	0.00		
		-	-	220kV BitDeer - Dagapela Line	56.60		
		-	-	5MVA, 220/33kV TFR	0.00		
<b>Total</b>	<b>0.00</b>	<b>Auxiliary Consumption &amp; Transformation Losses at Generator end</b>	<b>0.00%</b>				
8	4 x 15MW KHP	Unit-I	15.35	132kV KHP - Nangkhor Line	2.17	Unit-III & IV on Standby. Unit-II under Shutdown (AMP).	
		Unit-II	0.00	132kV KHP - Kihkhar Line	12.56		
		Unit-III	0.00	5MVA, 132/11kV TFR	0.55		
		Unit-IV	0.00	132kV Motanga - Rangia Line	-16.21		
		<b>Total</b>	<b>15.35</b>	<b>Auxiliary Consumption &amp; Transformation Losses at Generator end</b>	<b>0.46%</b>		
9	2 x 59MW NHP	Unit-I	15.00	132kV NHP-MHP-I	14.90	Unit II under AMP. 132kV NHP-MHP line II on ideal charge at MHP end.	
		Unit-II	0.00	132kV NHP-MHP-II	0.00		
		<b>Total</b>	<b>15.00</b>	<b>Auxiliary Consumption &amp; Transformation Losses at Generator end</b>	<b>0.67%</b>		
10	2 x 9MW SHP	Unit-I	0.00	66kV SHP-Damdhum (Samtse)	0.00	Unit-I on Standby. Interim measure: Evacuation is through 33kV System.	
		Unit-II	3.30	-	-		
		<b>Total</b>	<b>3.30</b>	<b>Auxiliary Consumption &amp; Transformation Losses at Generator end</b>	<b>100.00%</b>		

Note: Generation-Load Summary (MW) for 08-Mar-2026 at 18:00 hrs

Sl. No.	Region	Total Generation	Total Domestic Load (Total Generation - Total Export)	Total Export(+ve)/Import(-ve)
1	Both Eastern & Western (Whole Bhutan)	764.00	1,317.62	-553.62


Note: Generation-Load Summary (MW) for 08-Mar-2025, at 18:00 hrs

Sl. No.	Region	Total Generation	Total Domestic Load (Total Generation - Total Export)	Total Export(+ve)/Import(-ve)
1	Both Eastern & Western (Whole Bhutan)	898.70	869.79	29.31

Note: Daily Energy (MUs) and Power(MW) Statistics for 08-Mar-2026

Sl. No.	Total Energy Generation	Daily Energy Met	Net Energy Import (IEX and Solar)	Net Energy Export	Peak Cross-border (MW)
1	14.71	31.49	16.89	0.00	-1,019.33

**19:00 hrs Statistical Comparison (MW) for this and last year**

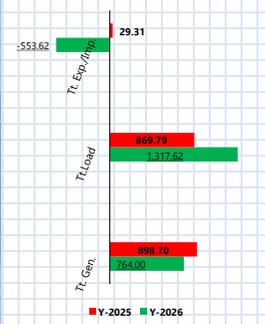

1. The Instantaneous load balance does not tend towards zero. This could be due to the following reasons:

- i) Not all the meters are digital and nor are all the meter at all locations can be read at same time (say 9:00hrs) due to many meter to be read manually. ii) The clocks of all the locations are not synchronized.
2. This report, compiled using the SCADA data, is prepared to give an overall idea of the generation & load flow for the system at a particular instant. This report also gives energy and import-export figures.
3. When SCADA data are unavailable for certain stations due to technical issues, required data are collected from the site.
